Water Well Digging & Construction Gaza

Progress Report 6



Project Name	Digging & Construction Water Well in Nuseirat
Project Location	Nuesirat
Name of Contractor	Waqnar Company for Contracting
Site Handover Date	15 th August 2016
Reporting period	April 2017

Capacity	Will pump out 60,000 litre / hour of water
No. of people benefiting	10,000



Section One: Project Description


Ummah Welfare Trust has installed a new water well at Al-Nuesirat which is a poor region of Gaza with a population of approximately 60,000 people.

Al- Nuseirat region is located far from water resources causing insufficient hydraulic pressure and quantity of water, especially in summer to supply households with running water.

The installation of a new water well in Nuseirat will improve the water and sanitation sector and ensure a continuous supply of water for the residents.

The installation includes excavation works, construction, supplying and installing of pipes and electro-mechanical works such electrical generators and distribution of boards and cables for operation.

The water well will be connected to the local water network distribution system at AI-Nuesirat

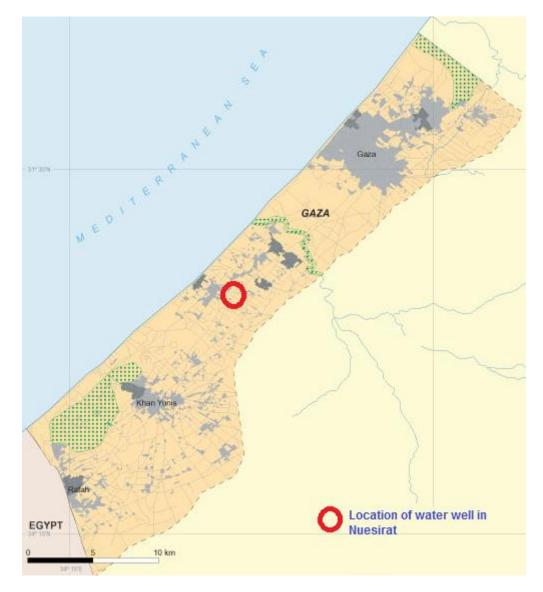

Location of Water Well in Nuseirat

Progress of Works

STAGE 1 Drilling Works		
1	Drilling and digging Borehole passing through any type of soil with diameter of min. 18 inches size	\checkmark
2	Supply and install steel pipes schedule 80. 12" diameter. 9.8 mm thickness from the top of the screen to the top of the well	\checkmark
3	Supply, weld and install a Stainless steel screen Grade 304, 12" diameter 5mm thick	\checkmark
4	Supply; weld and install Stainless steel pipe Grade 304 . 12" diameter 5 mm thick at the end of the filter	\checkmark
5	Supply and weld of stainless bottom plate of thickness 5 mm minimum 12" diameter	\checkmark
6	Supply and lower graded quartz (1.5-2.5) mm.	\checkmark
7	Transport to the site the contractors pumping equipment. Assembly and dismantling those equipment and cleaning the well by pumping	1
8	Pumping test and required measurement including detailed bacteriological and chemical analysis	\checkmark

STAGE 2 Civil & Construction Works		
1	Excavate for ground beams and foundations	٦
2	Supply and cast reinforced concrete for the ground beams and foundations	٦
3	Supply and cast reinforced concrete for the ground slab	٦
4	Supply and cast reinforced concrete for the columns	\checkmark
5	Supply and build hollow blocks size 20*20*40	\checkmark
6	Supply and cast reinforced concrete for Ribbed slabs cm thick	\checkmark
7	Dissociate wood and support for slab	۸
8	Establishment electrical works	۸
9	Supply and install local marble	٦
10	Supply and install galvanized steel doors and window	۸
11	Supply and execute internal plastering	٦
12	Supply and execute external plastering	1
13	Supply and install tiles for floor	۸
14	Supply and install internal and external plastering	۸

STAGE 3 Electromechanical Works		
1	Installation of water pumping unit	1
2	Installation of the pumping manifold	٦
3	Supply and install electrical works	\checkmark
4	Installation chlorine disinfection system	\checkmark
5	Supply & install UPVC pipes PN10, 110mm dia.,& connect with water network	Ā

Internal and external plastering has completed





Galvanized steel door and windows has completed





Electrical works has completed





Connection with water network has been installed

